Waterford School District 2016 Bond Program

Board Update– 09.17.2020

Barton Malow BUILDERS

AMERICAN OWNED

What Did We Do Last Summer?

Fun Facts

- 33,390 Work Hours
- At Peak of Construction 100 Contractors were on Site
- Worked on 9 Building District Wide
- 0 Safety Incidents, Accidents or Injuries
- Roughly $10 Million Put in Place in Construction

Barton Malow
BUILDERS

Schoolcraft Elementary

Phase 1 Summer 2020

- INTERIOR: New lights, ceilings, floors, etc. Boilers scheduled for start up 9/25
- EXTERIOR: New parking lot, bus loop, playground, underground utilities, etc._Playground equipment scheduled for delivery through the month of October. Equipment to be installed as it is delivered. Punch list walk through scheduled for 9/17
- ADDITION: New 9,000 SQFT gym addition. Duct work, electrical and masonry in progress scheduled for completion 12/31

Barton Malow
BUILDERS

Schoolcraft Elementary

Interior

Barton Malow
BUILDERS

Schoolcraft Elementary
Interior Continued

Barton Malow
BUILDERS

Schoolcraft Elementary
Interior Continued

Barton Malow
BUILDERS

Schoolcraft Elementary
Interior Continued

Barton Malow
BUILDERS

Schoolcraft Elementary

Exterior

Barton Malow
BUILDERS

Schoolcraft Elementary

Exterior Continued

Barton Malow
BUILDERS

Schoolcraft Elementary Addition

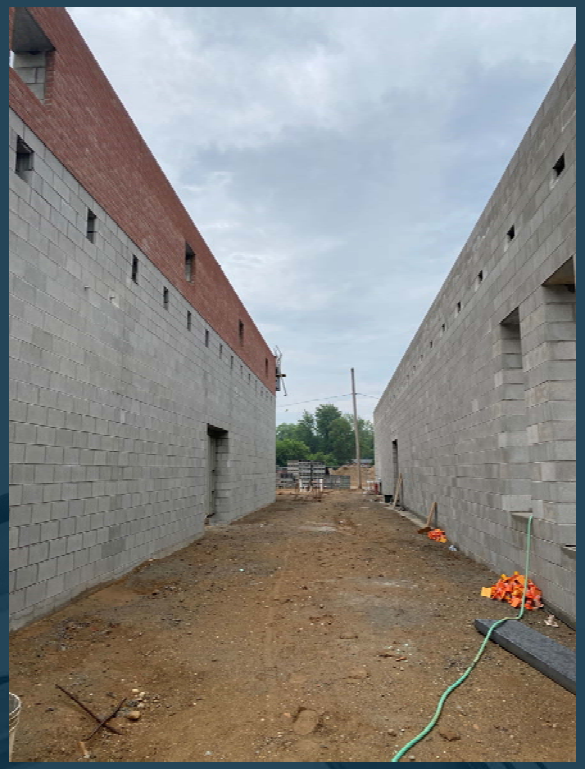

Barton Malow
BUILDERS

Schoolcraft Elementary Addition

Barton Malow
BUILDERS

Schoolcraft Elementary Addition

Barton Malow
BUILDERS

Schoolcraft Elementary
Phase 2 Summer 2021

- INTERIOR: New casework, classroom floors, etc.

Barton Malow
BUILDERS

Cooley Elementary
Phase 2 Summer 2020

- INTERIOR: New classroom floor, casework, etc. pending punch list walk through scheduled for 9/17

- EXTERIOR: Soccer field and site grading around addition in progress, pending punch list walk through scheduled for 9/17

- GYM ADDITION: Addition is complete, pending punch list walk through scheduled for 9/17

Barton Malow
BUILDERS

Cooley Elementary

Interior

Barton Malow
BUILDERS

Cooley Elementary
Interior Continued

Barton Malow
BUILDERS

Cooley Elementary
Interior Continued

Barton Malow
BUILDERS

Cooley Elementary Exterior

Beaumont Elementary
Phase 2 Summer 2020

- INTERIOR: New classroom floors, casework etc., pending punch list walk through scheduled for 9/17

- EXTERIOR: Complete pending punch list walk through scheduled for 9/17

Barton Malow
BUILDERS

Beaumont Elementary

Interior

Barton Malow
BUILDERS

Beaumont Elementary

Exterior

Grayson Elementary
Phase 2 Summer 2020

- INTERIOR: New classroom floors, casework etc., pending punch list walk through scheduled for 9/17

- EXTERIOR: Complete pending punch list walk through scheduled for 9/17

Barton Malow
BUILDERS

Grayson Elementary

Interior

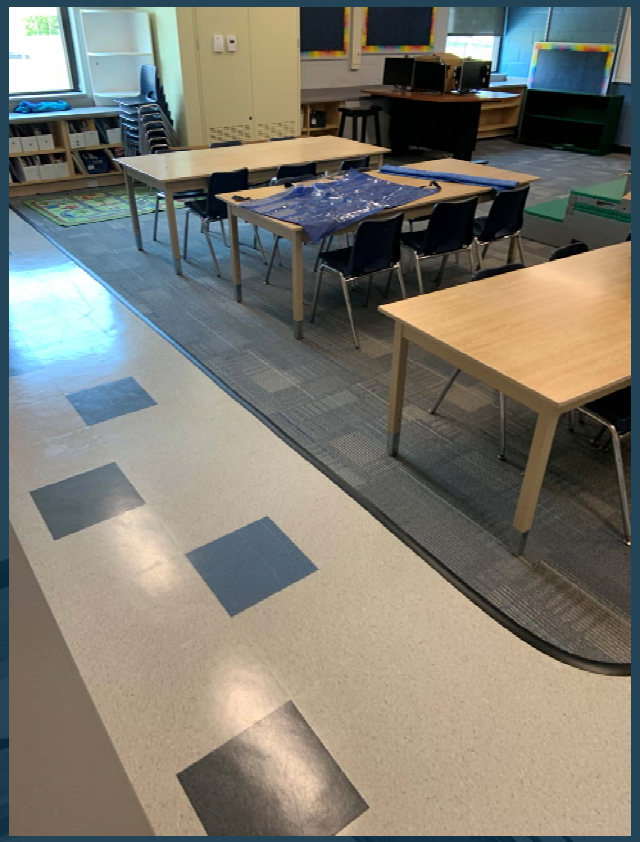

Barton Malow
BUILDERS

Grayson Elementary

Exterior

Other Projects

- MOTT: All piping tied in and operational with water to building, ready for occupancy. Ceilings and lights are complete pending punch list walk through scheduled for 9/17

- KETTERING: Concrete replacement and asphalt is complete per base bid, remaining concrete at Hatchery Rd. waiting for approval from Road Commission

- CRARY: Handrails Scheduled for Installation 9/28/2020, sidewalks and staircase are complete

Barton Malow
BUILDERS

Kettering High School
Exterior

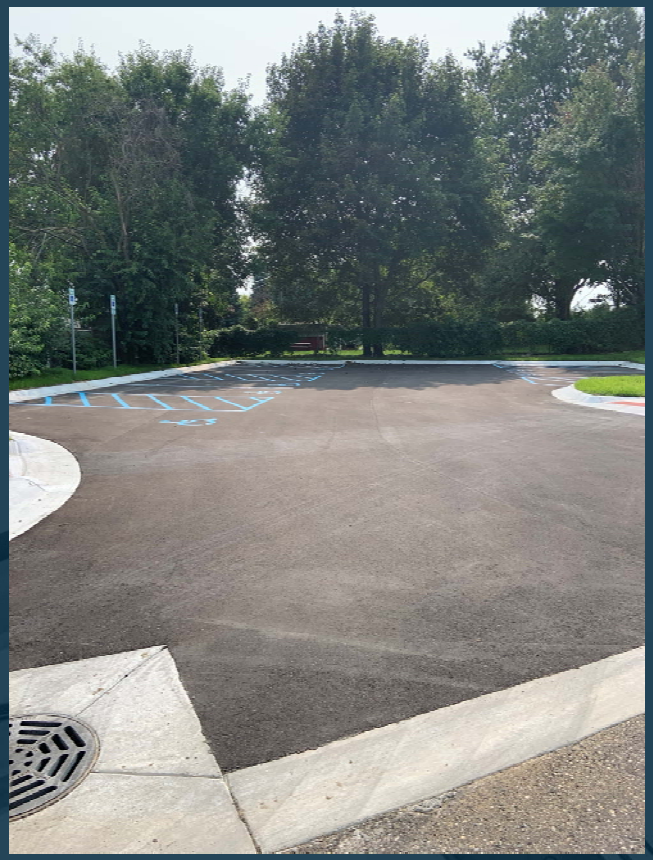

Barton Malow
BUILDERS

Kettering High School
Exterior Continued

Barton Malow
BUILDERS

Kurzman Administration Building

Exterior

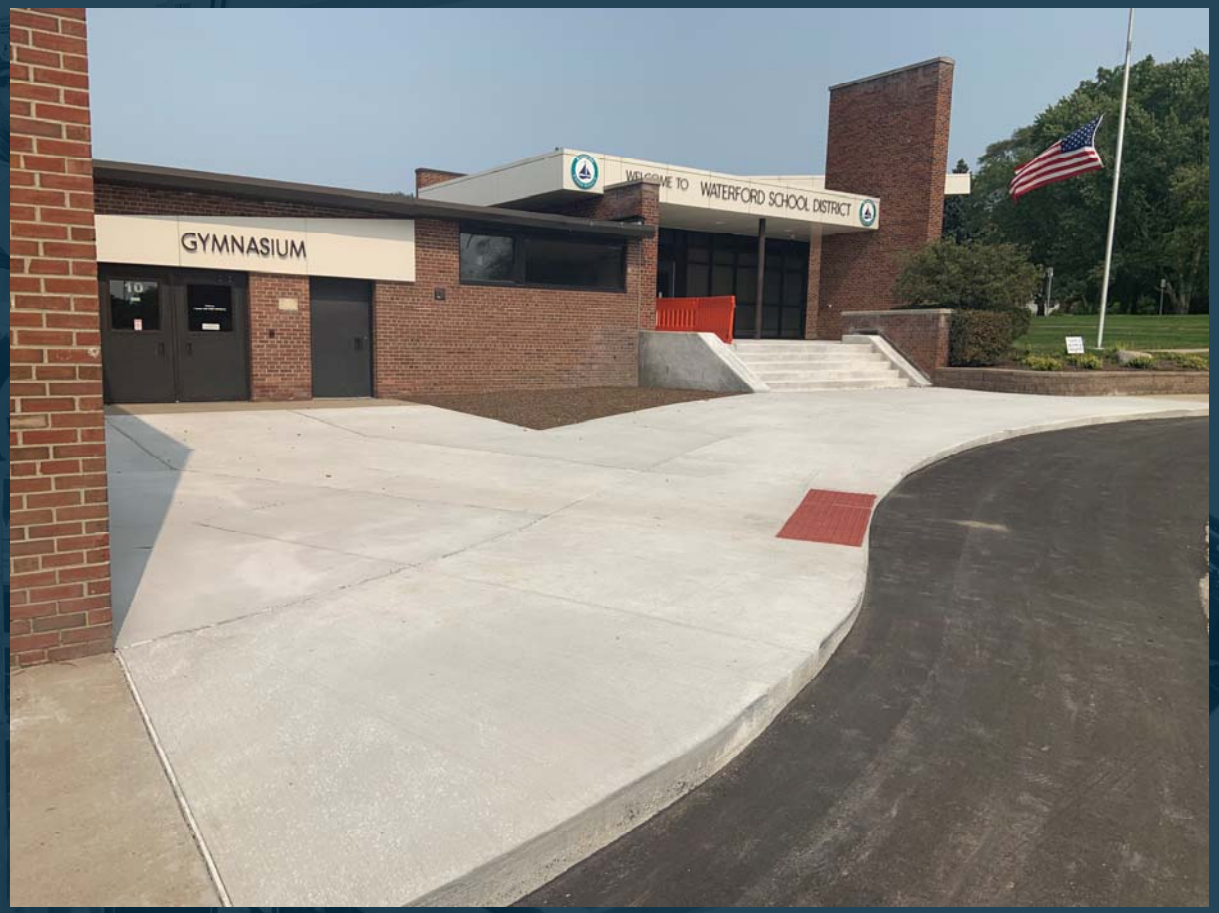

Thank you WSD for an Amazing
2020 Summer!
Barton Malow
BUILDERS
